


BUNKER HILL ROAD RECONSTRUCTION



BUNKER HILL ROAD RECONSTRUCTION

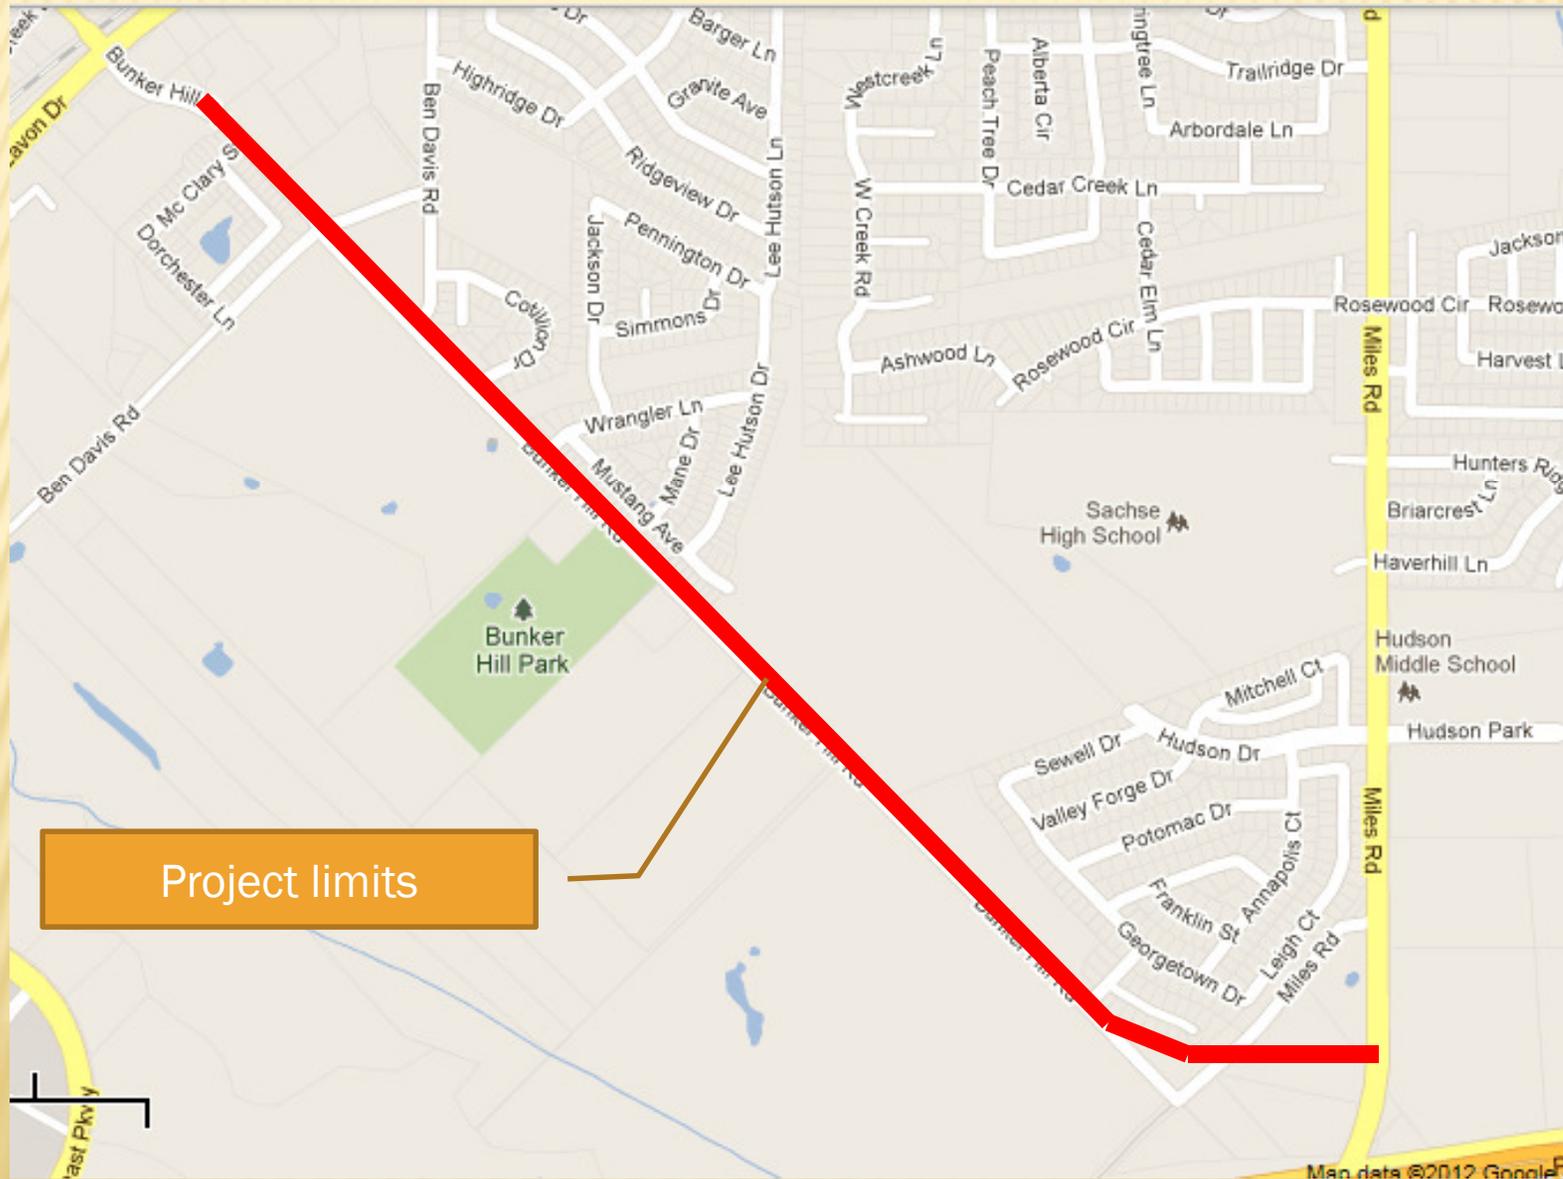

07.24.2012 15:52

BUNKER HILL ROAD RECONSTRUCTION



07.24.2012 15:03

BUNKER HILL ROAD RECONSTRUCTION



07.24.2012 15:07

BUNKER HILL ROAD RECONSTRUCTION

- + Project limits extend from south of SH 78 to Miles Road
- + Construction is approximately 85% complete
- + Contract cost is \$7,239,063 (funded using Regional Toll Revenue funds and 2006 Bond funds)
- + All utilities are complete
- + Paving is complete
- + Working on sidewalks, landscaping, irrigation system and parkway grading and clean up
- + Contract time ends January 2013 but project is four months ahead of schedule
